





SCHOOL DISTRICT OF NEW RICHMOND FACILITIES PROJECTS UPDATE JANUARY 2026



CONSTRUCTION PROGRESS

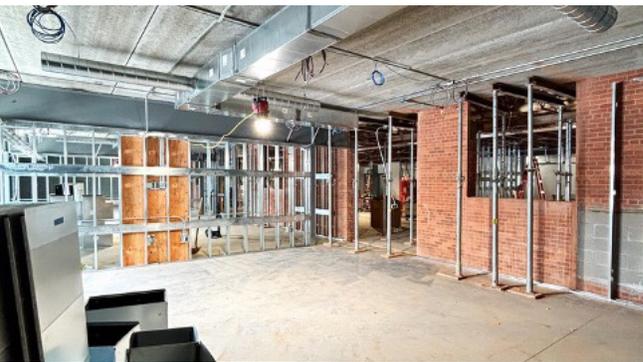

CONSTRUCTION PROGRESS

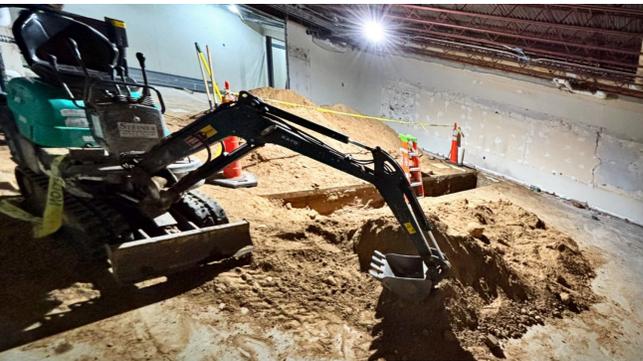

CONSTRUCTION PROGRESS



CONSTRUCTION PROGRESS

STARR ELEMENTARY

WORK COMPLETED

- Addition A Curtain Wall
- Addition D Curtain Wall
- Lower-Level Area A and Part of B
 - Abatement
 - Selective Demo
 - Mechanical Demo
 - Electrical Demo

WORK IN PROGRESS

- Lower-Level Area A and Part of B
 - Remaining Plumbing Demo
 - Window/Door Frames
 - Interior Framing
 - Above Ceiling MEP Rough-Ins
 - Hanging Drywall
 - Replacing Existing Sanitary Lines
 - Saw Cutting the Concrete Floor
 - Patching back the concrete

WORK UPCOMING

- Lower-Level Area A and Part of B
 - Tape/Mud/Sand Drywall
 - ACT Grid and Ceiling Tile Install
 - Painting Throughout
 - Polished Concrete Floors
 - MEP Finishes
 - Bathroom and Corridor Tile
 - Casework Install



SCAN HERE

to learn more about the referendum projects
